1st and final Bill

AEE/SSD/SBR/118/16-17 Dt: 29/9/2016

Est. cost :- 49.00 lakhs
Jobcode :- 018-17-000002

M.A.R. 57 (Rule 116)

Measurement Book No. C/09 168757

Construction of RCC drains at BHEL mini colony balance roads and 1st, 2nd, 3rd, 5th cross Serial No. near Hiremcharangaiah house all either (2) sides in ward No. 13, Shettyhalli sub division

Name of work..... From..... To..... B.A.No. 473/26 10

Name of Contractor of nature of Agency..... Technical Manager (West), KRIDL

A.A No :- AE/DZ/AS/31/2016-17 dt 30/9/16
T.S.No :- CE/DZ/TS/471/2016-17 dt. 01.09.16
W.O.No :- BBMP/EE/DD/WO/57/16-17 dt. 2/9/16

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Date of recording 19-9-16						
(1)	Earthwork excavation by manual means in ordinary soil involving an average horizontal throw upto 2m and an average lift upto 1.5m, excavated surface levelled and sides neatly dressed, the disposed earth to be levelled neatly after breaking of clods complete as per specifications.						
	As per premeasurement Qty recorded in this MB Page No. 168763 vide item no. (1)					540.52 Cum	
	@ Rate of 83.16/cum					= ₹ 44,950/-	
(2)	Providing and laying in position plain cement concrete of mix 1:4:8 with OPC cement @ 150 kgs, with 40mm and down						

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Cross road RTS	6	0.60	0.90		3.24	
	US	6	0.60	0.90		3.24	
	Cross road near Idea School	10	0.60	0.90		5.40	
	missed Slabs	118	0.60	0.90		63.72	
	Main Rd						
	Effect Rain Rd						
						138.24 Sqm	
	@ Rate ₹ 1600/Sqm					= ₹2,21,184/-	
(7)	Disposal of debris to the final place of disposal with all lead and lift and as direction by the engineer in charge of the works. lead 10 km						
	Qty vide Item no. (6)					540.52 Cum	
	@ Rate ₹ 81.73/Cum					= ₹44,177/-	
						4476089.00	
					Sub total	= ₹44,76,177/-	
					KRIDL @ 8%	= ₹ 3,58,094/-	
					@ 1%	= ₹ 49,000/-	
					Total	= ₹ 48,83,269/-	
						4834176.00	

Cl & Re

29/9/2016

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಶೆಟ್ಟಿಹಳ್ಳಿ ಉಪವಿಭಾಗ, ದಾಸರಹಳ್ಳಿ ವಲಯ
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ
ಎಸ್.ಎಂ ರಸ್ತೆ, ರವೀಂದ್ರನಗರ, ಬೆಂಗಳೂರು

EXECUTIVE ENGINEER-4
KRIDL, BBMP DIVISION
BENGALURU-560 010

Certified Rs 19-9-16

M.A.R. 57 (Rule 116) 4834176=00

Measurement Book No. C/09 168760

Audited and admitted for Rs.....

Passed by Cheque for Rs. 4194911=00

Serial No.....

Name of work..... From..... To.....

Name of Contractor of nature of Agency.....

Date of commencement of work..... by adjustment Rs. 639265=00

Accounts Superintendent Exe. Engineer

Date	Full description, etc, of work	Number	Dimensions Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
	Certificate: ① The works done by contractor satisfactorily. ② The contractor has removed all debris from worksite. ③ There is no departmental issues. ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು ಶೆಟ್ಟಿಹಳ್ಳಿ ಉಪವಿಭಾಗ, ದಾಸರಹಳ್ಳಿ ವಲಯ ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ ಎಸ್.ಎಂ ರಸ್ತೆ, ರವೀಂದ್ರನಗರ, ಬೆಂಗಳೂರು						

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8

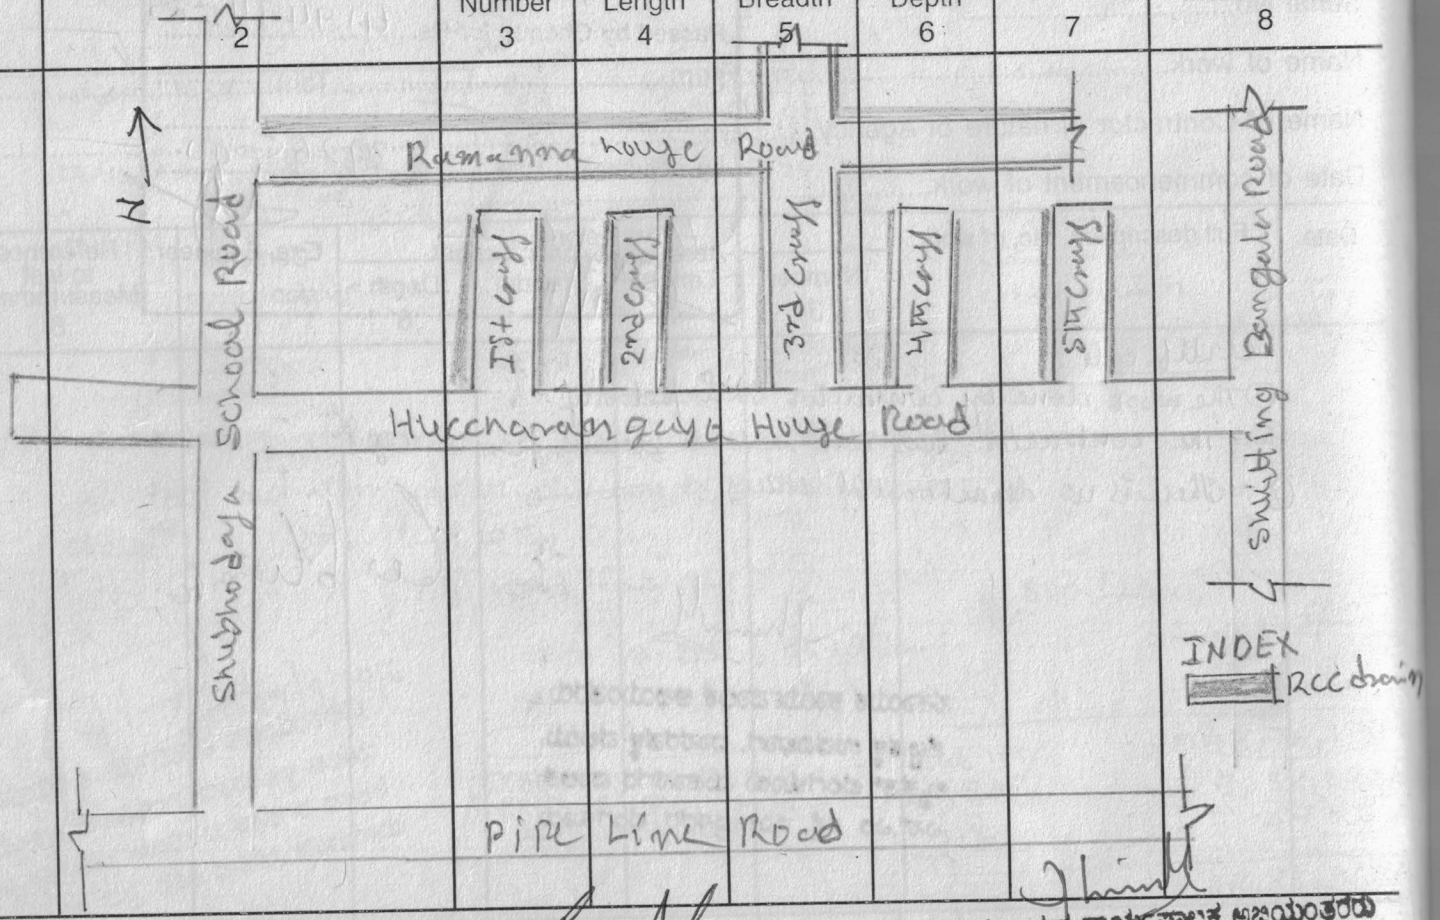

ಸಹಾಯಕ ಕಾರ್ಯ ಪಾಲಕ ಅಭಿಯಂತರರು
ಶಿಬ್ಬಹಳ್ಳಿ ಉಪವಿಭಾಗ, ದಾಸಕಹಳ್ಳಿ ವಲಯ
